

Detailed, Grouped by Each Number

Woodland High School	Project # 4113074-000	Skanska USA Building Inc.
	Tel: Fax:	

Date: 12/4/2013	Reference Number: 0007
------------------------	-------------------------------

Transmitted To:	Steve Broback McGranahan Architects 2111 Pacific Avenue, Suite 100 Tacoma, WA 98402 Tel: 253-383-3084 Fax: 253-383-3097	Transmitted By:	Brandon Jensen Skanska USA Building Inc. 222 SW Columbia Street, Suite 300 Portland, OR 97201 Tel: 503 382 0900 Fax: 503 382 0901
------------------------	--	------------------------	--

Qty	Submittal Package No	Description	Due Date	Package Action
1	0001 - 013250 - 0	Project Schedule Submittal	12/18/2013	

Transmitted For	Delivered Via	Tracking Number
Approval	Email	

Items	Qty	Description	Notes	Item Action
0001		Project Schedule		

Cc:	Company Name	Contact Name	Copies	Notes
-----	--------------	--------------	--------	-------

Remarks

Signature

Signed Date

Skanska USA Building, Inc.

Submittal: 013250-0001-0 Project Schedule.pdf

Date Received: 12/4/2013

To Architect: 12/4/2013

From Architect:


Returned to Sub:

This submittal REVIEW indicates that information presented conforms generally with the Contract Documents. In no case is Subcontractor or Supplier relieved of full responsibility for adherence to the Contract Documents and satisfactory construction of all work. Submitted to Owner, Architect-Engineer, for final approval.

Reviewed By: 

Date: 12/04/2013

Printed Name: Brandon Jensen

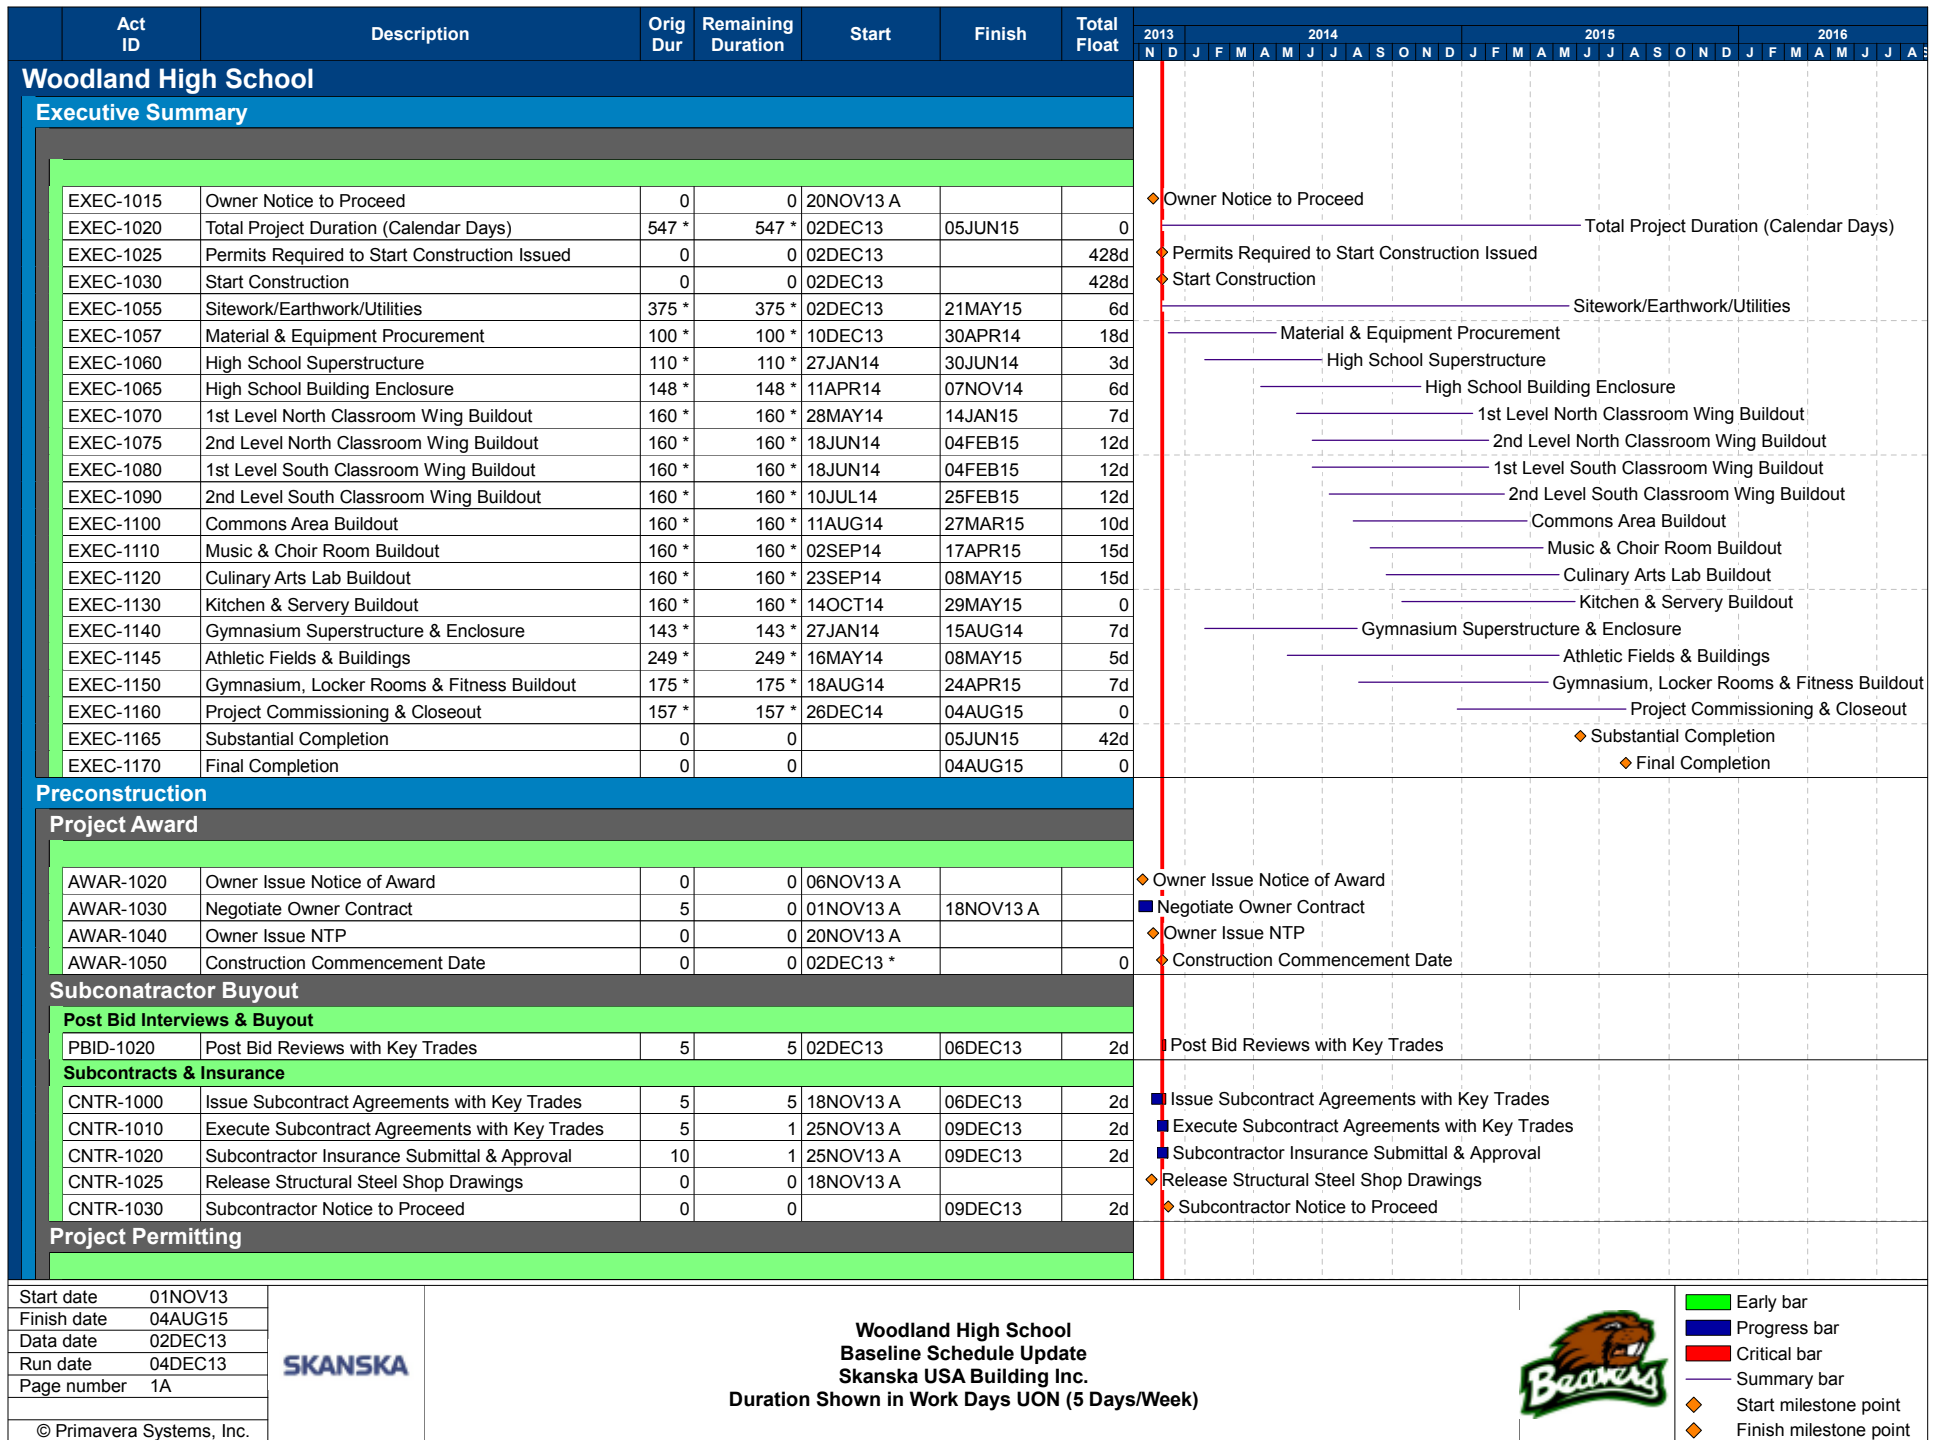

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	Gantt Chart																																															
								2013												2014												2015												2016											
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D										
	PERM-1000	Grading Permit - By Owner	0	0	27NOV13 A																																											Grading Permit - By Owner							
	PERM-1010	Storm Water Permit - By Owner	0	0	27NOV13 A																																											Storm Water Permit - By Owner							
	PERM-1020	FinalCorp. of Engineers Approval - By Owner	0	0	27NOV13 A																																											FinalCorp. of Engineers Approval - By Owner							
	PERM-1030	Building Permit	0	0	27NOV13 A																																											Building Permit							
Critical Material & Equipment Procurement																																																							
Subcontractor Submittal Development																																																							
	SUBM-0900	Storm & Sanitary Structures/Pipe Shop Drawings	5	5	10DEC13	16DEC13	27d	Storm & Sanitary Structures/Pipe Shop Drawings																																															
	SUBM-1000	Concrete Mix Designs	5	5	10DEC13	16DEC13	7d	Concrete Mix Designs																																															
	SUBM-1003	Geopier Shop Drawings	5	5	18NOV13 A	06DEC13	5d	Geopier Shop Drawings																																															
	SUBM-1005	Rebar Shop Drawings	5	5	10DEC13	16DEC13	2d	Rebar Shop Drawings																																															
	SUBM-1010	Masonry (CMU, Resteel, Grout Mixes, etc.)	5	5	10DEC13	16DEC13	14d	Masonry (CMU, Resteel, Grout Mixes, etc.)																																															
	SUBM-1040	Miscellaneous Metals (Embeds, Lintels, etc.)	5	5	10DEC13	16DEC13	3d	Miscellaneous Metals (Embeds, Lintels, etc.)																																															
	SUBM-1045	Structural Steel Shop Drawings - Area 1	20	12	18NOV13 A	17DEC13	0	Structural Steel Shop Drawings - Area 1																																															
	SUBM-1060	Structural Steel Shop Drawings - Area 2	20	20	02DEC13	30DEC13	13d	Structural Steel Shop Drawings - Area 2																																															
	SUBM-1070	Structural Steel Shop Drawings - Area 3	20	20	09DEC13	07JAN14	17d	Structural Steel Shop Drawings - Area 3																																															
	SUBM-1080	Structural Steel Shop Drawings - Area 4	20	20	16DEC13	14JAN14	20d	Structural Steel Shop Drawings - Area 4																																															
	SUBM-1090	Steel Joists & Decking	20	20	04DEC13	02JAN14	3d	Steel Joists & Decking																																															
	SUBM-1100	Mechanical Units (AHU's, RTU's, Boilers)	20	20	10DEC13	08JAN14	18d	Mechanical Units (AHU's, RTU's, Boilers)																																															
Skanska Submittal Review																																																							
	SKRV-0900	Storm & Sanitary Structures/Pipe Shop Drawings	5	5	17DEC13	23DEC13	27d	Storm & Sanitary Structures/Pipe Shop Drawings																																															
	SKRV-0905	Concrete Mix Designs	5	5	17DEC13	23DEC13	7d	Concrete Mix Designs																																															
	SKRV-0910	Rebar Shop Drawings	5	5	17DEC13	23DEC13	2d	Rebar Shop Drawings																																															
	SKRV-0915	Geopier Shop Drawings	1	1	09DEC13	09DEC13	5d	Geopier Shop Drawings																																															
	SKRV-1000	Masonry (CMU, Resteel, Grout Mixes, etc.)	5	5	17DEC13	23DEC13	14d	Masonry (CMU, Resteel, Grout Mixes, etc.)																																															
	SKRV-1040	Miscellaneous Metals (Embeds, Lintels, etc.)	5	5	17DEC13	23DEC13	3d	Miscellaneous Metals (Embeds, Lintels, etc.)																																															
	SKRV-1045	Structural Steel Shop Drawings - Area 1	5	5	18DEC13	24DEC13	0	Structural Steel Shop Drawings - Area 1																																															
	SKRV-1055	Structural Steel Shop Drawings - Area 2	5	5	31DEC13	07JAN14	13d	Structural Steel Shop Drawings - Area 2																																															
	SKRV-1065	Structural Steel Shop Drawings - Area 3	5	5	08JAN14	14JAN14	17d	Structural Steel Shop Drawings - Area 3																																															
	SKRV-1075	Structural Steel Shop Drawings - Area 4	5	5	15JAN14	21JAN14	20d	Structural Steel Shop Drawings - Area 4																																															
	SKRV-1085	Steel Joists & Decking	5	5	03JAN14	09JAN14	3d	Steel Joists & Decking																																															
	SKRV-1100	Mechanical Units (AHU's, RTU's, Boilers)	5	5	09JAN14	15JAN14	18d	Mechanical Units (AHU's, RTU's, Boilers)																																															
A/E Submittal Review & Approval																																																							
	AERV-0900	Storm & Sanitary Structures/Pipe Shop Drawings	15	15	24DEC13	15JAN14	27d	Storm & Sanitary Structures/Pipe Shop Drawings																																															
	AERV-0905	Concrete Mix Designs	15	15	24DEC13	15JAN14	7d	Concrete Mix Designs																																															
	AERV-0910	Rebar Shop Drawings	15	15	24DEC13	15JAN14	2d	Rebar Shop Drawings																																															
	AERV-0920	Geopier Shop Drawing Review	10	10	10DEC13	23DEC13	5d	Geopier Shop Drawing Review																																															
	AERV-1000	Masonry (CMU, Resteel, Grout Mixes, etc.)	20	20	24DEC13	22JAN14	14d	Masonry (CMU, Resteel, Grout Mixes, etc.)																																															
	AERV-1040	Miscellaneous Metals (Embeds, Lintels, etc.)	15	15	24DEC13	15JAN14	3d	Miscellaneous Metals (Embeds, Lintels, etc.)																																															
	AERV-1045	Structural Steel Shop Drawings - Area 1	15	15	26DEC13	16JAN14	0	Structural Steel Shop Drawings - Area 1																																															
	AERV-1055	Structural Steel Shop Drawings - Area 2	15	15	08JAN14	28JAN14	13d	Structural Steel Shop Drawings - Area 2																																															
	AERV-1065	Structural Steel Shop Drawings - Area 3	15	15	15JAN14	04FEB14	17d	Structural Steel Shop Drawings - Area 3																																															
	AERV-1075	Structural Steel Shop Drawings - Area 4	15	15	22JAN14	11FEB14	20d	Structural Steel Shop Drawings - Area 4																																															
	AERV-1085	Steel Joists & Decking	15	15	10JAN14	30JAN14	3d	Steel Joists & Decking																																															
	AERV-1100	Mechanical Units (AHU's, RTU's, Boilers)	15	15	16JAN14	05FEB14	18d	Mechanical Units (AHU's, RTU's, Boilers)																																															
Fabricate/Deliver Material & Equipment																																																							

Start date	01NOV13		Woodland High School Baseline Schedule Update Skanska USA Building Inc. Duration Shown in Work Days UON (5 Days/Week)		Early bar Progress bar Critical bar Summary bar Start milestone point Finish milestone point
Finish date	04AUG15				
Data date	02DEC13				
Run date	04DEC13				
Page number	2A				
© Primavera Systems, Inc.					

Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013												2014												2015												2016											
							N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D										
FABD-1000	Storm & Sanitary Structures/Pipe Shop Drawings	10	10	16JAN14	29JAN14	27d	Storm & Sanitary Structures/Pipe Shop Drawings																																															
FABD-1020	Rebar Fab/Deliver	5	5	16JAN14	22JAN14	2d	Rebar Fab/Deliver																																															
FABD-1030	Masonry (CMU, Resteel, Grout Mixes, etc.)	30	30	23JAN14	05MAR14	14d	Masonry (CMU, Resteel, Grout Mixes, etc.)																																															
FABD-1040	Miscellaneous Metals (Embeds, Lintels, etc.)	5	5	16JAN14	22JAN14	3d	Miscellaneous Metals (Embeds, Lintels, etc.)																																															
FABD-1045	Structural Steel Fab/Deliver - Area 1	30	30	17JAN14	27FEB14	0	Structural Steel Fab/Deliver - Area 1																																															
FABD-1055	Structural Steel Fab/Deliver - Area 2	30	30	29JAN14	11MAR14	13d	Structural Steel Fab/Deliver - Area 2																																															
FABD-1065	Structural Steel Fab/Deliver - Area 3	30	30	05FEB14	18MAR14	17d	Structural Steel Fab/Deliver - Area 3																																															
FABD-1075	Structural Steel Fab/Deliver - Area 4	30	30	12FEB14	25MAR14	20d	Structural Steel Fab/Deliver - Area 4																																															
FABD-1085	Steel Joists & Decking Fab/Deliver	30	30	31JAN14	13MAR14	3d	Steel Joists & Decking Fab/Deliver																																															
FABD-1100	Mechanical Units (AHU's, RTU's, Boilers)	60	60	06FEB14	30APR14	18d	Mechanical Units (AHU's, RTU's, Boilers)																																															
High School Construction																																																						
Mobilize																																																						
MOBI-1000	Start Mobilization	0	0	02DEC13		0	Start Mobilization																																															
MOBI-1030	Key Trade Preconstruction Meetings	3	3	02DEC13	04DEC13	0	Key Trade Preconstruction Meetings																																															
MOBI-1080	Construction Fencing & Signage	5	5	19DEC13	26DEC13	12d	Construction Fencing & Signage																																															
MOBI-1090	Job Trailer Setup	3	3	27DEC13	31DEC13	12d	Job Trailer Setup																																															
MOBI-1100	Mobilization Complete	0	0		31DEC13	12d	Mobilization Complete																																															
Site Prep Work																																																						
SPRP-1000	Start Site Prep	0	0	05DEC13		0	Start Site Prep																																															
SPRP-1010	Locate Existing Utilities	3	3	05DEC13	09DEC13	0	Locate Existing Utilities																																															
SPRP-1020	Establish Temporary Utilities	3	3	05DEC13	09DEC13	0	Establish Temporary Utilities																																															
SPRP-1030	Establish Soil Control Measures	5	5	05DEC13	11DEC13	0	Establish Soil Control Measures																																															
SPRP-1040	Initial Site Survey & Benchmarks	5	5	05DEC13	11DEC13	0	Initial Site Survey & Benchmarks																																															
SPRP-1050	Establish Construction Entrance	5	5	12DEC13	18DEC13	12d	Establish Construction Entrance																																															
SPRP-1060	Site Prep Work Complete	0	0		18DEC13	20d	Site Prep Work Complete																																															
Sitework & Utilities																																																						
Soil Surcharging																																																						
SRCH-1000	Phase 1 Surcharge Complete (Anticipated Date)	0	0	05DEC13		0	Phase 1 Surcharge Complete (Anticipated Date)																																															
SRCH-1020	Import/Infill Wetlands	15	15	05DEC13	26DEC13	0	Import/Infill Wetlands																																															
SRCH-1025	Transfer Material from Phase 1 to Phase 2	20	20	19DEC13	17JAN14	0	Transfer Material from Phase 1 to Phase 2																																															
SRCH-2020	Soil Surcharge Phase 2 - S. Parking Lot/Football	90	90	18JAN14	17APR14	10d	Soil Surcharge Phase 2 - S. Parking Lot/Football																																															
SRCH-2030	Transfer Material from Phase 2 to Fill Area	20	20	18APR14	15MAY14	6d	Transfer Material from Phase 2 to Fill Area																																															
SRCH-2040	Phase 2 Surcharge Complete	0	0		15MAY14	6d	Phase 2 Surcharge Complete																																															
Storm Water Detention Reservoirs																																																						
SDET-1000	Start Storm Water Detention Reservoirs	0	0	16MAY14		22d	Start Storm Water Detention Reservoirs																																															
SDET-1010	South Storm Water Detention Area	40	40	16MAY14	14JUL14	22d	South Storm Water Detention Area																																															
SDET-1020	North Storm Water Detention Area	40	40	13OCT14	09DEC14	6d	North Storm Water Detention Area																																															
SDET-1030	Detention Reservoirs Complete	0	0		09DEC14	6d	Detention Reservoirs Complete																																															
Establish Building Pad																																																						
BPAD-1000	Start Building Pad	0	0	20JAN14		0	Start Building Pad																																															
BPAD-1010	Establish School & Gymnasium Building Pad	5	5	20JAN14	24JAN14	0	Establish School & Gymnasium Building Pad																																															
BPAD-1020	Building Pad Complete	0	0		24JAN14	0	Building Pad Complete																																															

Start date01NOV13

Finish date04AUG15

Data date02DEC13

Run date04DEC13

Page number3A

© Primavera Systems, Inc.

Woodland High School

Baseline Schedule Update

Skanska USA Building Inc.

Duration Shown in Work Days UON (5 Days/Week)

Early bar

Progress bar

Critical bar

Summary bar

Start milestone point

Finish milestone point

Beavers

Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013	2014	2015	2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
LAND-1070	Landscaping Complete	0	0		21MAY15	6d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											</

Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013												2014												2015												2016											
							N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D										
Slab on Grade																																																						
SOG-1000	Start Slab on Grade Work	0	0	18APR14		0	◆ Start Slab on Grade Work																																															
SOG-1010	MEP U/G at N. Classroom Wing	10	10	18APR14	01MAY14	0	■ MEP U/G at N. Classroom Wing																																															
SOG-1015	Fine Grade SOG Subbase - N. Wing	3	3	01MAY14	05MAY14	0	■ Fine Grade SOG Subbase - N. Wing																																															
SOG-1040	F/R/P SOG - N. Classroom Wing	5	5	06MAY14	12MAY14	0	■ F/R/P SOG - N. Classroom Wing																																															
SOG-1050	MEP U/G at S. Classroom Wing	10	10	02MAY14	15MAY14	3d	■ MEP U/G at S. Classroom Wing																																															
SOG-1055	Fine Grade SOG Subbase - S. Wing	3	3	16MAY14	20MAY14	3d	■ Fine Grade SOG Subbase - S. Wing																																															
SOG-1060	F/R/P SOG - S. Classroom Wing	5	5	21MAY14	28MAY14	3d	■ F/R/P SOG - S. Classroom Wing																																															
SOG-1070	MEP U/G at Commons/Music/Kitchen	10	10	03JUN14	16JUN14	0	■ MEP U/G at Commons/Music/Kitchen																																															
SOG-1075	Fine Grade SOG Subbase - Commons/Music/Kitch.	3	3	13JUN14	17JUN14	0	■ Fine Grade SOG Subbase - Commons/Music/Kitch.																																															
SOG-1080	F/R/P SOG - Commons/Music/Kitchen	10	10	17JUN14	30JUN14	0	■ F/R/P SOG - Commons/Music/Kitchen																																															
SOG-1200	Slab On Grade Complete	0	0		30JUN14	3d	◆ Slab On Grade Complete																																															
Exterior Enclosure																																																						
Roofing																																																						
ROOF-1000	Start Roofing	0	0	11APR14		29d	◆ Start Roofing																																															
ROOF-1005	Install Roof Insulation/Plywood	40	40	11APR14	06JUN14	29d	■ Install Roof Insulation/Plywood																																															
ROOF-1010	Install Ice & Water Shield	30	30	19MAY14	30JUN14	18d	■ Install Ice & Water Shield																																															
ROOF-1020	Roof Dry-In	0	0		30JUN14	18d	◆ Roof Dry-In																																															
ROOF-1030	Install Roof Shingles	35	35	10JUN14	29JUL14	18d	■ Install Roof Shingles																																															
ROOF-1040	Roof Complete	0	0		29JUL14	18d	◆ Roof Complete																																															
West Elevation																																																						
EFRM-1000	Start Exterior Framing	0	0	13MAY14		4d	◆ Start Exterior Framing																																															
EFRM-1040	Install Exterior Framing	10	10	13MAY14	27MAY14	4d	■ Install Exterior Framing																																															
EFRM-1050	Install Exterior Sheathing	5	5	28MAY14	03JUN14	15d	■ Install Exterior Sheathing																																															
EFRM-1060	Install Ice & Water Shield	3	3	04JUN14	06JUN14	15d	■ Install Ice & Water Shield																																															
EFRM-1070	Install Exterior Insulation	5	5	09JUN14	13JUN14	15d	■ Install Exterior Insulation																																															
EFRM-1080	Install Exterior CMU Veneer	7	7	16JUN14	24JUN14	15d	■ Install Exterior CMU Veneer																																															
EFRM-1085	Wash Masonry Walls	2	2	25JUN14	26JUN14	15d	■ Wash Masonry Walls																																															
EFRM-1090	Install Metal Panels	10	10	27JUN14	11JUL14	15d	■ Install Metal Panels																																															
EFRM-1100	Install Windows & Caulking	10	10	14JUL14	25JUL14	15d	■ Install Windows & Caulking																																															
EFRM-1110	West Elevation Complete	0	0		25JUL14	15d	◆ West Elevation Complete																																															
North & South Wing Elevations																																																						
NSEL-1000	Start Exterior Framing	0	0	29MAY14		3d	◆ Start Exterior Framing																																															
NSEL-1010	Install Exterior Framing	20	20	29MAY14	25JUN14	3d	■ Install Exterior Framing																																															
NSEL-1020	Install Exterior Sheathing	10	10	26JUN14	10JUL14	7d	■ Install Exterior Sheathing																																															
NSEL-1030	Install Ice & Water Shield	6	6	11JUL14	18JUL14	7d	■ Install Ice & Water Shield																																															
NSEL-1040	Install Exterior Insulation	10	10	21JUL14	01AUG14	7d	■ Install Exterior Insulation																																															
NSEL-1050	Install Exterior CMU Veneer	14	14	04AUG14	21AUG14	7d	■ Install Exterior CMU Veneer																																															
NSEL-1060	Wash Masonry Walls	4	4	22AUG14	27AUG14	7d	■ Wash Masonry Walls																																															
NSEL-1070	Install Metal Panels	20	20	28AUG14	25SEP14	7d	■ Install Metal Panels																																															
NSEL-1080	Install Windows & Caulking	20	20	26SEP14	23OCT14	7d	■ Install Windows & Caulking																																															
NSEL-1090	North & South Elevation Complete	0	0		23OCT14	7d	◆ North & South Elevation Complete																																															
East Elevation																																																						
ESEL-1000	Start Exterior Framing	0	0	01JUL14		0	◆ Start Exterior Framing																																															
ESEL-1010	Install Exterior Framing	20	20	01JUL14	29JUL14	0	■ Install Exterior Framing																																															

Start date	01NOV13	SKANSKA	Woodland High School Baseline Schedule Update Skanska USA Building Inc. Duration Shown in Work Days UON (5 Days/Week)		Early bar
Finish date	04AUG15				Progress bar
Data date	02DEC13				Critical bar
Run date	04DEC13				Summary bar
Page number	6A				Start milestone point
© Primavera Systems, Inc.					Finish milestone point

Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013												2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							N D J F M A M J J A S O N D												J F M A M J J A S O N D												J F M A M J J A S O N D												J F M A M J J A S O N D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
ESEL-1020	Install Exterior Sheathing	5	5	30JUL14	05AUG14	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013201420152016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
								2013												2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
	NCW1-1240	Install Doors/Hardware	10	10	04DEC14	17DEC14	7d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		</

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013																											
								2014												2015												2016			
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F
	SCW1-4000	1st Floor South Classroom Wing Complete	0	0		04FEB15	12d	1st Floor South Classroom Wing Complete																											
	SCW1-4005	Install OF/OI Carpet & Base	10	10	08JUN15	19JUN15	32d	Install OF/OI Carpet & Base																											
	Commons Area Gridlines F-M/7-8																																		
	COMM-1000	Start Commons Area Buildout	0	0	11AUG14		0	Start Commons Area Buildout																											
	COMM-1010	Frame Interference Walls (walls w/adjacent MEP)	5	5	11AUG14	15AUG14	10d	Frame Interference Walls (walls w/adjacent MEP)																											
	COMM-1020	Hang & Fire Tape High Walls (Top GWB)	5	5	14AUG14	20AUG14	10d	Hang & Fire Tape High Walls (Top GWB)																											
	COMM-1030	O/H Electrical Install	15	15	21AUG14	11SEP14	10d	O/H Electrical Install																											
	COMM-1040	O/H HVAC Install	15	15	21AUG14	11SEP14	10d	O/H HVAC Install																											
	COMM-1050	O/H Overhead Plumbing	15	15	02SEP14	22SEP14	10d	O/H Overhead Plumbing																											
	COMM-1060	O/H Fire Sprinkler Install	10	10	09SEP14	22SEP14	10d	O/H Fire Sprinkler Install																											
	COMM-1070	Install Cable Tray	5	5	23SEP14	29SEP14	10d	Install Cable Tray																											
	COMM-1080	Frame Remaining Walls	15	15	23SEP14	13OCT14	10d	Frame Remaining Walls																											
	COMM-1090	In-wall Electrical R/I	15	15	30SEP14	20OCT14	10d	In-wall Electrical R/I																											
	COMM-1100	In-wall Plumbing R/I	15	15	30SEP14	20OCT14	10d	In-wall Plumbing R/I																											
	COMM-1110	In-Wall LSS R/I	5	5	14OCT14	20OCT14	10d	In-Wall LSS R/I																											
	COMM-1120	In-Wall LAN R/I (OF/OI)	5	5	14OCT14	20OCT14	10d	In-Wall LAN R/I (OF/OI)																											
	COMM-1140	Install Wall Backing	5	5	21OCT14	27OCT14	10d	Install Wall Backing																											
	COMM-1150	Final Wall Cover Inspection	0	0		27OCT14	10d	Final Wall Cover Inspection																											
	COMM-1160	H/T/F Drywall Partitions	15	15	28OCT14	17NOV14	10d	H/T/F Drywall Partitions																											
	COMM-1165	Install Hard Lid Framing	10	10	07NOV14	20NOV14	10d	Install Hard Lid Framing																											
	COMM-1170	Install Sprinkler Drops (Hard Lids)	8	8	21NOV14	04DEC14	15d	Install Sprinkler Drops (Hard Lids)																											
	COMM-1180	Install Light Fixture (Hard Lids)	10	10	21NOV14	08DEC14	10d	Install Light Fixture (Hard Lids)																											
	COMM-1190	Install Grilles/Diffusers (Hard Lids)	10	10	21NOV14	08DEC14	10d	Install Grilles/Diffusers (Hard Lids)																											
	COMM-1200	H/T/F Hard Lids	10	10	02DEC14	15DEC14	10d	H/T/F Hard Lids																											
	COMM-1210	Paint Walls	8	8	16DEC14	26DEC14	10d	Paint Walls																											
	COMM-1212	Install Stage & Ramp	20	20	29DEC14	26JAN15	16d	Install Stage & Ramp																											
	COMM-1220	Install Bathroom Tile	10	10	29DEC14	12JAN15	10d	Install Bathroom Tile																											
	COMM-1230	Install Ceiling Grid	10	10	29DEC14	12JAN15	10d	Install Ceiling Grid																											
	COMM-1240	O/H Projector R/I (OF/OI)	5	5	13JAN15	19JAN15	14d	O/H Projector R/I (OF/OI)																											
	COMM-1250	Install Casework	10	10	13JAN15	26JAN15	10d	Install Casework																											
	COMM-1260	Install Light Fixtures (ACT)	10	10	13JAN15	26JAN15	10d	Install Light Fixtures (ACT)																											
	COMM-1270	Install Grilles/Diffusers (ACT)	10	10	13JAN15	26JAN15	10d	Install Grilles/Diffusers (ACT)																											
	COMM-1280	Install Sprinkler Drops (ACT)	10	10	13JAN15	26JAN15	10d	Install Sprinkler Drops (ACT)																											
	COMM-1290	Install Flooring	10	10	27JAN15	09FEB15	10d	Install Flooring																											
	COMM-1310	Fixture Trim Out	15	15	27JAN15	16FEB15	14d	Fixture Trim Out																											
	COMM-1315	Install Acoustical Ceiling Panel System	15	15	27JAN15	16FEB15	16d	Install Acoustical Ceiling Panel System																											
	COMM-1317	Install Stage Curtain System	10	10	27JAN15	09FEB15	29d	Install Stage Curtain System																											
	COMM-1320	LAN Equipment Trim-out (OF/CI)	10	10	03FEB15	16FEB15	14d	LAN Equipment Trim-out (OF/CI)																											
	COMM-1330	Install Projectors (OF/OI)	10	10	03FEB15	16FEB15	14d	Install Projectors (OF/OI)																											
	COMM-1340	Install Accessories	10	10	17FEB15	02MAR15	14d	Install Accessories																											
	COMM-1343	Drop Ceiling Tile	10	10	17FEB15	02MAR15	14d	Drop Ceiling Tile																											
	COMM-1355	Install Theater Seating System	8	8	17FEB15	26FEB15	16d	Install Theater Seating System																											
	COMM-1360	Install Doors/Hardware	10	10	18FEB15	03MAR15	10d	Install Doors/Hardware																											
	COMM-1370	Install Signage	3	3	04MAR15	06MAR15	10d	Install Signage																											
	COMM-1380	Skanska/Subcontractor Pre-Punchlist	15	15	09MAR15	27MAR15	10d	Skanska/Subcontractor Pre-Punchlist																											

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013	2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
CULINARY ARTS LAB	COMM-4000	Commons Area Complete	0	0		27MAR15	10d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013	2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
CULINARY ARTS LAB BUILDOUT	CULI-1000	Start Culinary Arts Lab Buildout	0	0	23SEP14		0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013												2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
							N D J F M A M J J A S O N D												N D J F M A M J J A S O N D												J F M A M J J A S O N D												J F M A M J J A S O N D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
KITC-1045	O/H HVAC Install	15	15	24OCT14	13NOV14	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						

[illegible]

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	2013	2014												2015												2016																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
	SCW2-1190	Install Grilles/Diffusers (Hard Lids)	10	10	22OCT14	04NOV14	12d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

[illegible]

	Act ID	Description	Orig Dur	Remaining Duration	Start	Finish	Total Float	Gantt Chart																																					
								2013	2014												2015												2016												
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
	TRCK-1070	Running Track Complete	0	0		30APR15	11d	◆ Running Track Complete																																					
	Baseball & Softball Fields																																												
	Baseball Fields Grading & Seeding																																												
	BSBL-1000	Start Baseball Fields	0	0	02FEB15		5d	◆ Start Baseball Fields																																					
	BSBL-1020	Import Engineered Fill & Topsoil	20	20	02FEB15	27FEB15	5d	■ Import Engineered Fill & Topsoil																																					
	BSBL-1030	Install Irrigation System	15	15	02MAR15	20MAR15	7d	■ Install Irrigation System																																					
	BSBL-1040	Fine Grade Topsoil	10	10	23MAR15	03APR15	7d	■ Fine Grade Topsoil																																					
	BSBL-1050	Seed Field	5	5	06APR15	10APR15	7d	■ Seed Field																																					
	BSBL-1060	Baseball Field Seeding Complete	0	0		10APR15	7d	◆ Baseball Field Seeding Complete																																					
	Batting Cages																																												
	BTNG-1000	Start Batting Cages	0	0	02MAR15		5d	◆ Start Batting Cages																																					
	BTNG-1010	Buildout Batting Cages	50	50	02MAR15	08MAY15	5d	■ Buildout Batting Cages																																					
	BTNG-1020	Batting Cages Complete	0	0		08MAY15	5d	◆ Batting Cages Complete																																					
	Dugouts, Bleachers & Backstops																																												
	SEAT-1000	Start Dugouts, Bleachers & Backstops	0	0	02MAR15		5d	◆ Start Dugouts, Bleachers & Backstops																																					
	SEAT-1010	Buildout Dugouts, Bleachers & Backstops	50	50	02MAR15	08MAY15	5d	■ Buildout Dugouts, Bleachers & Backstops																																					
	SEAT-1020	Dugouts, Bleachers & Backstops Complete	0	0		08MAY15	5d	◆ Dugouts, Bleachers & Backstops Complete																																					
	Project Closeout																																												
	Substantial Completion																																												
	Commissioning																																												
	CMSG-1000	Start Commissioning	0	0	26DEC14		0	◆ Start Commissioning																																					
	CMSG-1010	MEP Equipment Startup & Commissioning	115	115	26DEC14	05JUN15	0	■ MEP Equipment Startup & Commissioning																																					
	CMSG-1020	MEP Commissioing Complete	0	0		05JUN15	0	◆ MEP Commissioing Complete																																					
	Punchlist																																												
	PNCH-1000	A/E Develop Punchlist	5	5	01JUN15	05JUN15	0	■ A/E Develop Punchlist																																					
	PNCH-1005	Final Inspection by AHJ	5	5	01JUN15	05JUN15	0	■ Final Inspection by AHJ																																					
	PNCH-1010	Substantial Completion	0	0		05JUN15	0	◆ Substantial Completion																																					
PNCH-1020	Punchlist (Calendar Days)	30	30	06JUN15	05JUL15	0	■ Punchlist (Calendar Days)																																						
PNCH-1030	Project Closeout (Calendar Days)	60	60	06JUN15	04AUG15	0	■ Project Closeout (Calendar Days)																																						
Final Completion & Turnover																																													
Owner Move-in & Occupancy																																													
OWNR-1010	Final Completion	0	0		04AUG15	0	◆ Final Completion																																						
