

Change Order Log						Bid amount	\$ 43,538,000.00
Woodland High School						Current	\$ 44,709,068.34
No.	Issue Date	COP# COR#	Type/ Cause	Description Pricing	Amount Approved	Sub Amount	
#001	12/18/2013	COP 001	A	Add Emergency Eye Wash	\$ 2,264.00		
		COP 002	B	Change elevator and Shaft	\$ 2,846.00		
							\$ 5,110.00
#002	2/11/2014	CCD 002	G	Pot hole for Geo grid	\$ 5,161.00		
		COP 007	C	Plumbing Changes at Culinary Arts Casework	\$ 4,012.00		
		COR 009	B	Extend Sanitary to Grandstand RFI#36	\$ 643.00		
		COR 012	C	Below Grade Vents per RFI#26 and RFI#29	\$ 1,746.00		
		COR 019	C	Double Welded Columns RFI041 (half of cost)	\$ 793.06		
		COR 020	C	Columns Location at Gridline L/14 RFI#042 (half of cost)	\$ 528.50		
		COR 021	B	Electrical Service Questions per RFI #49	\$ 4,895.00		
		COR 026	G	Geogrid Repair at Footings per RFI #61	\$ 1,127.78		
							\$ 18,906.34
#003	3/12/2014	CCD 004	A	Add Bentonite Under Elevator Pit	\$ 1,199.00		
		CCD 008	B	COP 011 4" CMU at Veneer Starter Course	\$ (4,113.00)		
		COP 003	B	Delta 4 Changes	\$ (3,426.00)		
		COP 004	B	PUD Service Changes	\$ -		
		COP 008	B	Change Extent of Perforated Roof Deck	\$ -		
		COP 012	B	Change Door 1401CB	\$ (2,326.00)		
		COP 014	B	Change Cross-Vent Blocking to 1 1/2" Thick	\$ 4,976.00		
		COP 015	B	Change Plumbing at Culinary Arts Hand Sinks	\$ (611.00)		
		COR 022	G	Nutter Geogrid Costs	\$ 6,512.00		
		COR 023	B	Delete 10 Dilution Tanks	\$ (1,143.00)		
		COR 027	B	RFI#52 Roof Drain Connection	\$ 4,711.00		
		COR 032	B	RFI#67 1/8" Slope for Plumbing	\$ (1,736.00)		
		COR 034	C	Detailing Costs for Bent Plate at Canopy	\$ 2,346.00		
		COR 035	C	Change Duct Routing at Hoist Beam RFI#093	\$ 1,356.00		
		COR 040	B	Oil Water Separator Elevation	\$ 4,411.00		
							\$ 12,156.00
#004	4/15/2014		A	Accept Alt. No 2 Synthetic Turf Field	\$ 525,000.00		
							\$ 525,000.00
#005	4/29/2014	CCD 06R1	C	Service Yard Utilities	\$ 19,237.00		
		CCD 009	B	Sanitary Sewer Modifications RFI 125	\$ 1,480.00		
		CCD 010	B	Add Camber to beams	\$ 1,083.00		



		CCD 013	F	CMU reinforcement RFI 136	\$ 2,244.00	
		COP 009R1	B	Power to Curtain and Operable Panel Partition	\$ 1,516.00	
		COP 010	B	Thickened Slab Edge at gyms	\$ (1,170.00)	
		COP 013	C	Rack and Panel move at IDF at Gyms	\$ 15,077.00	
		COR 050	C	Brace Frame Footing RFI# 140	\$ 342.00	
		COR 057	C	Fire Protection Line at Service yard Door	\$ 1,283.00	
		COR 058	B	Additional Joist Loading at N and S classroom wings	\$ 8,529.00	
						\$ 49,621.00
#006	5/28/2014	CCD 014/COR 061	B	Reinforcing for 6" Gym Walls	\$ 2,202.00	
		CCD 014/COR 065	B	Cope and install Web Stiffener	\$ 1,487.00	
		CCD 015	B	Eave Connection at K/5	\$ 1,621.00	
		CCD 017	A	Self Adhered Roof Underlayment	\$ 24,278.00	
		CCD 018	B	Roof Edge Sheathing	\$ 1,998.00	
		CCD 021/COP 027	A	Clay Traps at 3D art Room	\$ 1,929.00	
		COP 005	B	Delete Rebar	\$ (2,163.00)	
		COP 016	B	Steel Lintel at Gym Mechanical	\$ 1,712.00	
		COP 026	A	Add seismic shut off valve at gas meter	\$ 2,593.00	
		COR 066	B	Roof Hatch Clarification	\$ 321.00	
		COR 069	B	Washing Machine Connection	\$ 1,329.00	
		COR 073	F	Shut Off Valves for NPCW and NPHW	\$ 1,501.00	
		COR 074	B	Pipe Size Clarification RFI #226	\$ (3,153.00)	
		COR 077	C	Beam at Ships Ladder	\$ 2,200.00	
						\$ 37,855.00
#007		CCD 016	B	Changes to Storm Piping and footings	\$ 1,166.00	
		CCD 020	B	Modify berm at SW pond (no cost change)	\$ -	
		CCD 021/COR 92	B	Ice Maker Connections	\$ 3,143.00	
		CCD 024	A	Rift Cut door faces	\$ 5,343.00	
		COP 021	A	Revisions to entry mats	\$ (4,482.00)	
		COP 022R1	B	NPCW piping to HWT-2	\$ 3,472.00	
		COR 033	E	Weather delay	\$ 11,358.00	
		COR 046	B	Additional joist loading at Commons and Gyms	\$ 5,358.00	
		COR 067	C	GRS Conduit per RFI 155	\$ 1,086.00	
		COR 81	B	trench Drain at Loading Dock	\$ 1,117.00	
		COR 83R1	B	Add plumbing connections for 12 dishwashers	\$ 5,543.00	
		COR 086	B	Cooler drain in Room 1409B RFI 248	\$ 2,202.00	
		COR 087	B	Area drains and storm pipe RFI 224	\$ 1,526.00	
		COR 088	B	Install dilution tank at fume hood	\$ 141.00	
		COR 090	C	95% compaction at ball fields	\$ 3,122.00	




	COR 091	C	Door frame mod at Auxiliary gym	\$ 1,113.00	
					\$ 41,208.00
#008	CCD 003R1	D	Raise footings above geogrid	\$ 225,236.00	
					\$ 225,236.00
#009		A	Change concrete floors to polish finish	\$ 71,512.00	
					\$ 71,512.00
#010	CCD-025	B	Provide PT plywood at window heads RFI #262.	\$ 5,410.00	
	COP-019R	B	Cabinets at Science Classroom Plumbing	\$ -	
	COP-024	B	Owner requested casework modifications and additions	\$ (8,903.00)	
	COR-063	C	Additional framing costs RFI #133.	\$ 3,381.00	
	COR-095	B	Storm transition civil to landscape per RFI #271.	\$ 721.00	
	COR-118	B	Modify the wall assembly at the mechanical platform RFI #334.	\$ 436.00	
					\$ 1,045.00
#011	CCD-001	E	RFI#040 ROW Conflict with Power and Sewer	\$ 3,360.00	
	CCD-026	B	Aluminum Closure Angle at Sills	\$ 2,832.00	
	CCD-027	B	Wall Roof Joist Framing RFI 286	\$ 8,923.00	
	CCD-028	B	COP#017 2 hour Wall Changes	\$ 35,379.00	
	CCD-029	C	Exterior Brace Frame GWB	\$ 1,296.00	
	CCD-029	C	Handrail Bracket Revisions COP-030	\$ 2,106.00	
	CCD-029	C	Interior Wall at Brace Frame RFI-325	\$ 1,589.00	
	CCD-030	A	Digital AV System	\$ 35,786.00	
	CCD-031	A	Horticultural Lab Hose Bib	\$ 6,964.00	
	CCD-033	C	Aluminum Frame Location at Aux Gym RFI-265.1	\$ 3,233.00	
	CCD-038	C	Door Frame Depth Clarification RFI-278	\$ 2,874.00	
	CCD-034	B	Grandstand Ticket Booth Roof Drain Connections	\$ 14,610.00	
	CCD-037	B	Grandstand CMU Control Joints	\$ 6,853.00	
	CCD-035	B	Integrated Door Opening Pockets	\$ 2,172.00	
	CCD-036	B	HSS Column at Louver Opening COP-031	\$ 2,644.00	
	CCD-032	B	Steel shims at top of Gym walls	\$ 1,560.00	
	CCD-038	C	Waste riser realignment at Library	\$ 1,447.00	
					\$ 133,628.00
#012	COP-029	B	Track and Field Changes - COR 143	\$ -	
	COP-037	B	Court Stripping Changes - COR 133	\$ -	
	COP-033	C	Duct work changes at Commons - COR 123	\$ 3,256.00	
	COP-038	B	Hose bib and floor drain at Floral Lab	\$ 2,454.00	
	COR-116	A	Goal Post lettering - RFI 312	\$ 327.00	
	COR-124	B	Culinary arts sink - RFI 391	\$ 1,624.00	
	COR-137	B	Ceiling Fan support Brackets - RFI-391	\$ 4,734.00	



	COR-149	B	Exterior grade push bars at courtyard gate - RFI-374	\$ 615.00	
	COR-151	C	Adjustments at Mech Mezz framing - RFI-372	\$ 459.00	
					\$ 13,469.00
#013	CCD-011	C	Housekeeping pad relocation COR 152, RFI 145	\$ 777.00	
	CCD-042	B	Revise steel lintels at louvers; COR 115, RFI 297	\$ 1,615.00	
	CCD-044	B	Increase stud size to accommodate steel framing; COR 146, RFI 4	\$ 560.00	
	CCD-048	B	Provide IR device in Room 2407; COR 135, RFI 394	\$ 1,857.00	
	CCD-048	B	Provide power for ice mach., DW's; COR 153, RFI 442	\$ 3,986.00	
	CCD-053	C	Notch steel beam to accommodate door frame; COR 158	\$ 1,302.00	
	CCD-054	F	Relocate electrical transformer; COR 170, RFI 473	\$ 9,223.00	
	CCD-055	C	Relocate AHU-11; COR 161	\$ 2,576.00	
	CCD-055	B	Provide fire proofing at top of gym wall; COR 178, RFI 410	\$ 2,845.00	
	CCD-056	B	Provide steel bent plate at locker room wall; COR 154	\$ 4,202.00	
	COR-064	C	Relocate Aux gym access controls	\$ 1,969.00	
	COR-104	B	Supply (6) scoreboard columns	\$ 6,770.00	
	COR-129	A	Install scoreboard truss	\$ 1,964.00	
	COR-141	B	Change out GWB fire safing to rock wool at top of exterior walls	\$ (4,753.00)	
	COR-152	B	Add cabinet at Rooms 1208 and 2209	\$ 359.00	
	COR-162	A	Add bug screen to roof vents	\$ 1,070.00	
					\$ 36,322.00
			Total Change Orders		\$ 1,171,068.34
			Contingency Budget		\$ 2,251,883.00
			Contingency Balance	48.00%	\$ 1,080,814.66
			Source code:		
		A	Owner Requested Change	\$ 675,747	57.70%
		B	Design Team Coordination/value added	\$ 149,092	12.73%
		C	Design Team Coordination/non-value added	\$ 80,507	6.87%
		D	Geo-grid/Footings Revisions	\$ 225,236	19.23%
		E	Concealed/Unforeseen Condition	\$ 14,718	1.26%
		F	Code Required Change	\$ 12,968	1.11%
		G	Other	\$ 12,801	1.09%
				\$ 1,171,068	100.00%



Change Order Types

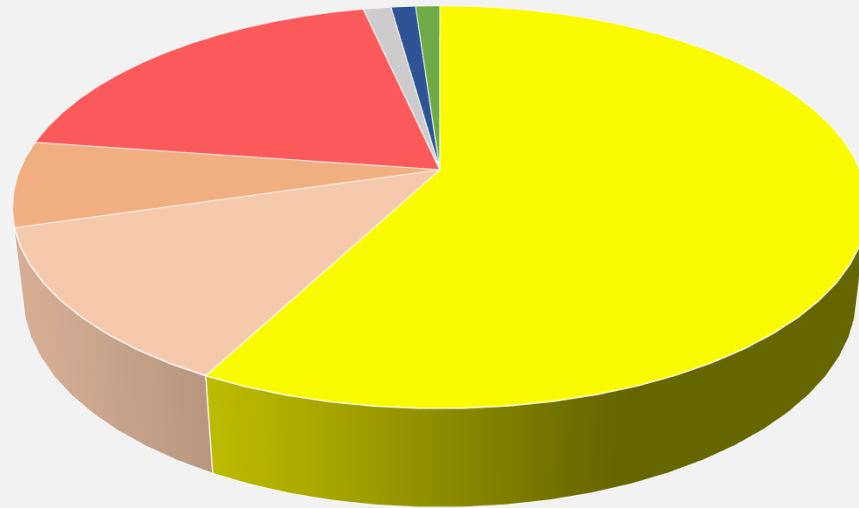

■ *Owner Requested Change*

■ *Design Team Coordination/non-value added*

■ *Concealed/Unforeseen Condition*

■ *Other*

■ *Design Team Coordination/value added*

■ *Geo-grid/Footings Revisions*

■ *Code Required Change*
